

# PMI

## Exam Questions CAPM

Certified Associate in Project Management (PMI-100)



#### NEW QUESTION 1

- (Exam Topic 3)

A work package has been scheduled to cost \$1,000 to complete and was to be finished today. As of today, the actual expenditure is \$1,200 and approximately half of the work has been completed. What is the cost variance?

- A. -700
- B. -200
- C. 200
- D. 500

**Answer:** A

#### NEW QUESTION 2

- (Exam Topic 3)

Change requests are an output from which Project Integration Management process?

- A. Direct and Manage Project Execution
- B. Develop Project Management Plan
- C. Close Project
- D. Develop Project Charter

**Answer:** A

#### NEW QUESTION 3

- (Exam Topic 3)

Which is an example of Administer Procurements?

- A. Negotiating the contract
- B. Authorizing contractor work
- C. Developing the statement of work
- D. Establishing evaluation criteria

**Answer:** B

#### NEW QUESTION 4

- (Exam Topic 3)

Which of the following is an output of the Define Activities process?

- A. Activity list
- B. Project plan
- C. Activity duration estimates
- D. Project schedule

**Answer:** A

#### NEW QUESTION 5

- (Exam Topic 3)

Which enterprise environmental factors are considered during Estimate Costs?

- A. Market conditions and published commercial information
- B. Company structure and market conditions
- C. Commercial information and company structure
- D. Existing human resources and market conditions

**Answer:** A

#### NEW QUESTION 6

- (Exam Topic 3)

An input to the Create WBS process is a:

- A. project charter.
- B. stakeholder register.
- C. project scope statement.
- D. requirements traceability matrix.

**Answer:** C

#### NEW QUESTION 7

- (Exam Topic 3)

Which type of contract is most commonly used by buying organizations because the price for goods is set at the outset and is not subject to change unless the scope of work changes?

- A. Fixed Price with Economic Price Adjustments Contract (FP-EPA)
- B. Cost-Reimbursable Contract (CR)
- C. Firm-Fixed -Price Contract (FFP)

D. Fixed-Price-Incentive-Fee Contract (FPIF)

**Answer:** C

**NEW QUESTION 8**

- (Exam Topic 3)

Which type of analysis systemically gathers and analyzes qualitative and quantitative information to determine which interests should be taken into account throughout the project?

- A. Product
- B. Cost-benefit
- C. Stakeholder
- D. Research

**Answer:** C

**NEW QUESTION 9**

- (Exam Topic 3)

Managing ongoing production of goods and services to ensure business continues efficiently describes which type of management?

- A. Portfolio
- B. Project
- C. Program
- D. Operations

**Answer:** D

**NEW QUESTION 10**

- (Exam Topic 3)

Which is the Define Scope technique used to generate different approaches to execute and perform the work of the project?

- A. Build v
- B. buy
- C. Expert judgment
- D. Alternatives identification
- E. Product analysis

**Answer:** C

**NEW QUESTION 10**

- (Exam Topic 3)

The approaches, tools, and data sources that will be used to perform risk management on a project are determined by the:

- A. Methodology
- B. Risk category
- C. Risk attitude
- D. Assumption analysis

**Answer:** A

**NEW QUESTION 13**

- (Exam Topic 3)

What is the function of a Project Management Office (PMO)?

- A. To focus on the coordinated planning, prioritization, and execution of projects and subprojects that are tied to the parent organizations or the client's overall business objectives.
- B. To coordinate and manage the procurement of projects relevant to the parent organization's business objectives and to administer the project charters accordingly.
- C. To administer performance reviews for the project manager and the project team members and to handle any personnel and payroll issues.
- D. To focus on the specified project objectives and to manage the scope, schedule, cost, and quality of the work packages.

**Answer:** A

**NEW QUESTION 16**

- (Exam Topic 3)

Conflict should be best addressed in which manner?

- A. Early, in private, using a direct, collaborative approach
- B. Early, in public, using an indirect, collaborative approach
- C. Early, in private, using an indirect, cooperative approach
- D. As late as possible, in public, using a direct, confrontational approach

**Answer:** A

**NEW QUESTION 19**

- (Exam Topic 3)

What is an objective of the Develop Project Team process?

- A. Feelings of trust and improved cohesiveness
- B. Ground rules for interaction
- C. Enhanced resource availability
- D. Functional managers becoming more involved

**Answer:** A

#### **NEW QUESTION 24**

- (Exam Topic 3)

Work performance information and cost forecasts are outputs of which Project Cost Management process?

- A. Estimate Costs
- B. Plan Cost Management
- C. Determine Budget
- D. Control Costs

**Answer:** D

#### **NEW QUESTION 26**

- (Exam Topic 3)

Most experienced project managers know that:

- A. every project requires the use of all processes in the PMBOK® Guide.
- B. there is no single way to manage a project.
- C. project management techniques are risk free.
- D. there is only one way to manage projects successfully.

**Answer:** B

#### **NEW QUESTION 28**

- (Exam Topic 3)

While implementing an approved change, a critical defect was introduced. Removing the defect will delay the product delivery. What is the MOST appropriate approach to managing this situation?

- A. Utilize the change control process.
- B. Crash the schedule to fix the defect.
- C. Leave the defect in and work around it.
- D. Fast-track the remaining development.

**Answer:** A

#### **NEW QUESTION 32**

- (Exam Topic 3)

Organizations perceive risks as:

- A. events that will inevitably impact project and organizational objectives.
- B. the effect of uncertainty on their project and organizational objectives.
- C. events which could have a negative impact on project and organizational objectives.
- D. the negative impact of undesired events on their project and organizational objectives.

**Answer:** B

#### **NEW QUESTION 35**

- (Exam Topic 3)

Cost baseline is an output of which of the following processes?

- A. Control Costs
- B. Determine Budget
- C. Estimate Costs
- D. Estimate Activity Resources

**Answer:** B

#### **NEW QUESTION 40**

- (Exam Topic 3)

Which of the seven basic quality tools is especially useful for gathering attributes data while performing inspections to identify defects?

- A. Histograms
- B. Scatter diagrams
- C. Flowcharts
- D. Checksheets

**Answer:** D

**NEW QUESTION 43**

- (Exam Topic 3)

Which organizational process assets update is performed during the Close Procurements process?

- A. Procurement audit
- B. Lessons learned
- C. Performance reporting
- D. Payment requests

**Answer: B**

**NEW QUESTION 46**

- (Exam Topic 3)

A collection of projects managed as a group to achieve strategic objectives is referred to as a:

- A. plan
- B. process
- C. program
- D. portfolio

**Answer: D**

**NEW QUESTION 48**

- (Exam Topic 3)

Definitions of probability and impact, revised stakeholder tolerances, and tracking are components of which subsidiary plan?

- A. Cost management plan
- B. Quality management plan
- C. Communications management plan
- D. Risk management plan

**Answer: D**

**NEW QUESTION 52**

- (Exam Topic 3)

What is the number of stakeholders, if the project has 28 potential communication channels?

- A. 7
- B. 8
- C. 14
- D. 16

**Answer: B**

**NEW QUESTION 55**

- (Exam Topic 3)

The project management processes presented in the PMBOK Guide® should:

- A. always be applied uniformly.
- B. be selected as appropriate by the sponsor.
- C. be selected as appropriate by the project team.
- D. be applied based on ISO guidelines.

**Answer: C**

**NEW QUESTION 56**

- (Exam Topic 3)

Projects are undertaken by an organization to support the:

- A. Product performance.
- B. Budget process.
- C. Collective capabilities.
- D. Organizational strategy.

**Answer: D**

**NEW QUESTION 59**

- (Exam Topic 3)

Projects can be divided into phases to provide better management control. Collectively, what are these phases known as?

- A. Complete project phase
- B. Project life
- C. The project life cycle
- D. Project cycle

**Answer: C**

#### NEW QUESTION 60

- (Exam Topic 3)

When an activity cannot be estimated with a reasonable degree of confidence, the work within the activity is decomposed into more detail using which type of estimating?

- A. Bottom-up
- B. Parametric
- C. Analogous
- D. Three-point

**Answer:** A

#### NEW QUESTION 64

- (Exam Topic 3)

A measure of cost performance that is required to be achieved with the remaining resources in order to meet a specified management goal and is expressed as the ratio of the cost needed for finishing the outstanding work to the remaining budget is known as the:

- A. budget at completion (BAC)
- B. earned value management (EVM)
- C. to-complete performance index
- D. cost performance index

**Answer:** C

#### NEW QUESTION 66

- (Exam Topic 3)

In an organization with a projectized organizational structure, who controls the project budget?

- A. Functional manager
- B. Project manager
- C. Program manager
- D. Project management office

**Answer:** B

#### NEW QUESTION 68

- (Exam Topic 3)

What type of project structure is a hierarchically organized depiction of the resources by type?

- A. Organizational breakdown structure (OBS)
- B. Resource breakdown structure (RBS)
- C. Work breakdown structure (WBS)
- D. Project breakdown structure (PBS)

**Answer:** B

#### NEW QUESTION 72

- (Exam Topic 3)

A project management office manages a number of aspects including the:

- A. Project scope, schedule, cost, and quality of the products of the work packages.
- B. Central coordination of communication management across projects.
- C. Assignment of project resources to best meet project objectives.
- D. Overall risk, overall opportunity, and interdependencies among projects at the enterprise level.

**Answer:** D

#### NEW QUESTION 73

- (Exam Topic 3)

Which of the following is a tool and technique for Estimate Activity Durations?

- A. Parametric estimating
- B. Monte Carlo analysis
- C. Alternatives analysis
- D. Bottom-up estimating

**Answer:** A

#### NEW QUESTION 76

- (Exam Topic 3)

What is one of the objectives of Project Risk Management?

- A. Decrease the probability and impact of an event on project objectives.
- B. Distinguish between a project risk and a project issue so that a risk mitigation plan can be put in place.
- C. Increase the probability and impact of positive events.
- D. Removal of project risk.

**Answer:** C

**NEW QUESTION 77**

- (Exam Topic 3)

The individual or group that provides resources and support for a project and is accountable for success is the:

- A. sponsor
- B. customer
- C. business partners
- D. functional managers

**Answer:** A

**NEW QUESTION 81**

- (Exam Topic 3)

What is the name of the statistical method that helps identify which factors may influence specific variables of a product or process under development or in production?

- A. Failure modes and effects analysis
- B. Design of experiments
- C. Quality checklist
- D. Risk analysis

**Answer:** B

**NEW QUESTION 83**

- (Exam Topic 3)

Which is a tool or technique used in Define Scope?

- A. Templates, forms, and standards
- B. Change requests
- C. Product analysis
- D. Project assumptions

**Answer:** C

**NEW QUESTION 85**

- (Exam Topic 3)

The creation of an internet site to engage stakeholders on a project is an example of which type of communication?

- A. Push
- B. Pull
- C. Interactive
- D. Iterative

**Answer:** B

**NEW QUESTION 86**

- (Exam Topic 3)

To which process is work performance information an input?

- A. Administer Procurements
- B. Direct and Manage Project Execution
- C. Create WBS
- D. Perform Qualitative Risk Analysis

**Answer:** A

**NEW QUESTION 88**

- (Exam Topic 3)

When can pre-assignment of project team members occur?

- A. When the project uses capital expenditures
- B. When the required staff can be acquired from outside sources
- C. When the project would be ignored due to travel expenses
- D. When the project is the result of specific people being promised as part of a competitive proposal

**Answer:** D

**NEW QUESTION 91**

- (Exam Topic 3)

Sharing good practices introduced or implemented in similar projects in the organization and/or industry is an example of:

- A. quality audits
- B. process analysis

- C. statistical sampling
- D. benchmarking

**Answer:** A

**NEW QUESTION 96**

- (Exam Topic 3)

The CPI is .92, and the EV is US\$172,500. What is the actual cost of the project?

- A. US\$158,700
- B. US\$172,500
- C. US\$187,500
- D. US\$245,600

**Answer:** C

**NEW QUESTION 98**

- (Exam Topic 3)

Plan Risk Management is the process of defining how to:

- A. Communicate identified risks to the project stakeholders.
- B. Conduct risk management activities for a project.
- C. Analyze the impact a specific risk may have on the project.
- D. Address unexpected risks that may occur during a project.

**Answer:** B

**NEW QUESTION 99**

- (Exam Topic 3)

Which technique should a project manager use in a situation in which a collaborative approach to conflict management is not possible?

- A. Coaching
- B. Avoidance
- C. Consensus
- D. Influencing

**Answer:** B

**NEW QUESTION 102**

- (Exam Topic 3)

An output of Control Schedule is:

- A. A project schedule network diagram
- B. A schedule management plan
- C. Schedule data
- D. Schedule forecasts

**Answer:** D

**NEW QUESTION 107**

- (Exam Topic 3)

Which Process Group's purpose is to track, review, and regulate the progress and performance of the project; identify any areas in which changes to the plan are required; and initiate the corresponding changes?

- A. Monitoring and Controlling
- B. Initiating
- C. Planning
- D. Executing

**Answer:** A

**NEW QUESTION 110**

- (Exam Topic 3)

When is a project finished?

- A. After verbal acceptance of the customer or sponsor
- B. After lessons learned have been documented in contract closure
- C. When the project objectives have been met
- D. After resources have been released

**Answer:** C

**NEW QUESTION 115**

- (Exam Topic 3)

Which of the following risk response strategies involves allocating ownership of a positive risk to a third party?



- A. Mitigate
- B. Transfer
- C. Share
- D. Avoid

**Answer:** C

**NEW QUESTION 118**

- (Exam Topic 3)

The formal and informal interaction with others in an organization industry, or professional environment is known as:

- A. negotiation
- B. organizational theory
- C. meeting
- D. networking

**Answer:** D

**NEW QUESTION 121**

- (Exam Topic 3)

Information collected on the status of project activities being performed to accomplish the project work is known as what?

- A. Project management information system
- B. Work performance information
- C. Work breakdown structure
- D. Variance analysis

**Answer:** B

**NEW QUESTION 125**

- (Exam Topic 2)

An example of a group decision-making technique is:

- A. nominal group technique
- B. majority
- C. affinity diagram
- D. multi-criteria decision analysis

**Answer:** B

**NEW QUESTION 128**

- (Exam Topic 2)

At the completion of a project, a report is prepared that details the outcome of the research conducted on a global trend during the project. Which item did this project create?

- A. Result
- B. Product
- C. Service
- D. Improvement

**Answer:** A

**NEW QUESTION 132**

- (Exam Topic 2)

Which output is the approved version of the time-phased project budget?

- A. Resource calendar
- B. Scope baseline
- C. Trend analysis
- D. Cost baseline

**Answer:** D

**NEW QUESTION 133**

- (Exam Topic 2)

Retreating from an actual or potential conflict or postponing the issue to be better prepared or to be resolved by others describes which of the five general techniques for managing conflict?

- A. Smooth/accommodate
- B. Withdraw/avoid
- C. Compromise/reconcile
- D. Force/direct

**Answer:** B

**NEW QUESTION 138**

- (Exam Topic 2)

High-level project risks are included in which document?

- A. Business case
- B. Risk breakdown structure
- C. Project charter
- D. Risk register

**Answer: C**

#### **NEW QUESTION 143**

- (Exam Topic 2)

A disadvantage associated with virtual teams is that they:

- A. Require communication technology that is not readily available.
- B. Create difficulties when including people with disabilities.
- C. Often cannot accommodate teams that work different hours or shifts.
- D. Create the possibility for misunderstandings to arise.

**Answer: D**

#### **NEW QUESTION 144**

- (Exam Topic 2)

Which term describes an assessment of correctness?

- A. Accuracy
- B. Precision
- C. Grade
- D. Quality

**Answer: A**

#### **NEW QUESTION 148**

- (Exam Topic 2)

When closing a project or phase, part of the process may require the use of which type of analysis?

- A. Reserve analysis
- B. Regression analysis
- C. Document analysis
- D. Product analysis

**Answer: B**

#### **NEW QUESTION 150**

- (Exam Topic 2)

A graphic display of project team members and their reporting relationships is known as a:

- A. Resource calendar.
- B. Project organization chart.
- C. Resource breakdown structure (RBS).
- D. Responsibility assignment matrix (RAM).

**Answer: B**

#### **NEW QUESTION 153**

- (Exam Topic 2)

A project team attempts to produce a deliverable and finds that they have neither the expertise nor the time to complete the deliverable in a timely manner. This issue could have been avoided if they had created and followed a:

- A. risk management plan
- B. human resource management plan
- C. scope management plan
- D. procurement management plan

**Answer: D**

#### **NEW QUESTION 157**

- (Exam Topic 2)

Which document in the project management plan can be updated in the Plan Procurement Management process?

- A. Budget estimates
- B. Risk matrix
- C. Requirements documentation
- D. Procurement documents

**Answer: C**

#### NEW QUESTION 160

- (Exam Topic 2)

In project management, a temporary project can be:

- A. Completed without planning
- B. A routine business process
- C. Long in duration
- D. Ongoing to produce goods

**Answer:** C

#### NEW QUESTION 163

- (Exam Topic 2)

A complete set of concepts, terms, and activities that make up an area of specialization is known as:

- A. a Knowledge Area
- B. a Process Group
- C. program management
- D. portfolio management

**Answer:** A

#### NEW QUESTION 165

- (Exam Topic 2)

Which Project Time Management process includes bottom-up estimating as a tool or technique?

- A. Estimate Activity Resources
- B. Sequence Activities
- C. Estimate Activity Durations
- D. Develop Schedule

**Answer:** A

#### NEW QUESTION 167

- (Exam Topic 2)

Activity cost estimates and the project schedule are inputs to which Project Cost Management process?

- A. Estimate Costs
- B. Control Costs
- C. Plan Cost Management
- D. Determine Budget

**Answer:** D

#### NEW QUESTION 171

- (Exam Topic 2)

The following chart contains information about the tasks in a project.

Task	PV	AC	EV
1	10,000	10,000	10,000
2	10,000	8,000	10,000
3	10,000	8,000	8,000
4	9,000	12,000	10,000
5	10,000	12,000	12,000
6	10,000	10,000	12,000
7	12,000	12,000	10,000
8	10,000	8,000	9,000
9	12,000	10,000	11,000

Based on the chart, what is the cost variance (CV) for Task 6?

- A. -2,000
- B. 1,000
- C. 2,000

**Answer:** D

#### NEW QUESTION 175

- (Exam Topic 2)

The following chart contains information about the tasks in a project.

Task	PV	AC	EV
1	10,000	10,000	10,000
2	10,000	8,000	10,000
3	10,000	8,000	8,000
4	9,000	12,000	10,000
5	10,000	12,000	12,000
6	10,000	10,000	12,000
7	12,000	12,000	10,000
8	10,000	8,000	9,000
9	12,000	10,000	11,000

Based on the chart, what is the schedule variance (SV) for Task 8?

A. A.--2,000B.-1,000C.1,000D.2,000

**Answer:** B

#### NEW QUESTION 176

- (Exam Topic 2)

The chart below is an example of a:

ID	Requirements Description	Project Objectives	WBS Deliverables	Product Design	Product Development	Test Cases
001						
002						
003						

- A. Responsibility assignment matrix (RAM)
- B. Work breakdown structure (WBS)
- C. RACI chart
- D. Requirements traceability matrix

**Answer:** D

#### NEW QUESTION 181

- (Exam Topic 2)

Which is an enterprise environmental factor?

- A. Marketplace conditions
- B. Policies and procedures
- C. Project files from previous projects
- D. Lessons learned from previous projects

**Answer:** A

#### NEW QUESTION 186

- (Exam Topic 2)

Requirements documentation will typically contain at least:

- A. Stakeholder requirements, staffing requirements, and transition requirements.
- B. Business requirements, the stakeholder register, and functional requirements.
- C. Stakeholder impact, budget requirements, and communications requirements.
- D. Business objectives, stakeholder impact, and functional requirements.

**Answer:** D

#### NEW QUESTION 189

- (Exam Topic 2)

The purpose of the Project Communications Management Knowledge Area is to:

- A. Monitor and control communications throughout the entire project life cycle.
- B. Maintain an optimal flow of information among all project participants.

- C. Develop an appropriate approach for project communications.
- D. Ensure timely and appropriate collection of project information.

**Answer:** D

**NEW QUESTION 194**

- (Exam Topic 2)

A project manager requesting industry groups and consultants to recommend project intervention is relying on:

- A. Communication models.
- B. Stakeholder participation.
- C. Expert judgment
- D. Enterprise environmental factors.

**Answer:** C

**NEW QUESTION 198**

- (Exam Topic 2)

Completion of the product scope is measured against the product:

- A. prototypes
- B. requirements
- C. analyses
- D. benchmarks

**Answer:** B

**NEW QUESTION 201**

- (Exam Topic 2)

In the Plan Procurement Management process, which source selection criteria analyzes if the seller's proposed technical methodologies, techniques, solutions, and services meet the procurement documents requirements?

- A. Technical approach
- B. Technical capability
- C. Business size and type
- D. Production capacity and interest

**Answer:** A

**NEW QUESTION 203**

- (Exam Topic 2)

The Project Human Resource Management process that involves confirming human resource availability and obtaining the team necessary to complete project activities is:

- A. Acquire Project Team.
- B. Plan Human Resource Management.
- C. Manage Project Team.
- D. Develop Project Team.

**Answer:** A

**NEW QUESTION 208**

- (Exam Topic 2)

An issue log is an input to which Project Human Resource Management process?

- A. Manage Project Team
- B. Acquire Project Team
- C. Plan Human Resource Management
- D. Develop Project Team

**Answer:** A

**NEW QUESTION 211**

- (Exam Topic 2)

Project Stakeholder Management focuses on:

- A. project staff assignments
- B. project team acquisition
- C. managing conflicting interests
- D. communication methods

**Answer:** C

**NEW QUESTION 212**

- (Exam Topic 2)

Project managers who lead by example and follow through on the commitments they make demonstrate the key interpersonal skill of:

- A. influencing
- B. leadership
- C. motivation
- D. coaching

**Answer:** A

#### NEW QUESTION 214

- (Exam Topic 2)

Which process involves the creation of a document that provides the project manager with the authority to apply resources to a project?

- A. Define Activities
- B. Direct and Manage Project Work
- C. Develop Project Management Plan
- D. Develop Project Charter

**Answer:** D

#### NEW QUESTION 218

- (Exam Topic 2)

One of the key benefits of the Plan Human Resource Management process is that it:


- A. outlines team selection guidelines and team member responsibilities.
- B. establishes project roles and responsibilities.
- C. improves teamwork, interpersonal skills, and competencies.
- D. provides an accurate appraisal of team member performance.

**Answer:** B

#### NEW QUESTION 221

- (Exam Topic 2)

The following is a network diagram for a project.

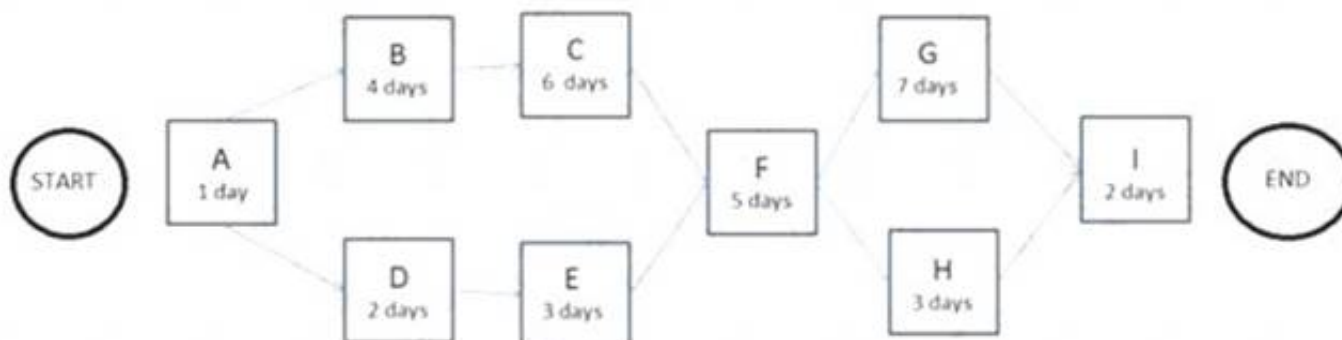

The free float for Activity E is how many days?

- A. 2
- B. 3
- C. 5
- D. 8

**Answer:** C

#### NEW QUESTION 223

- (Exam Topic 2)

Success is measured by benefits realization for a:

- A. strategic plan
- B. project
- C. portfolio
- D. program

**Answer:** C

#### NEW QUESTION 228

- (Exam Topic 2)

Which tool or technique used in the Control Procurements process can be conducted during the execution of the project to verify compliance with deliverables?

- A. Procurement documents
- B. Inspection and audits
- C. Estimate budget
- D. Risk register

**Answer:** B

#### NEW QUESTION 229



- (Exam Topic 2)

In the Define Activities process, the schedule management plan is used to:

- A. Capture the lessons learned from other projects for comparison.
- B. Contain the standard activity list.
- C. Document and support the project change requests.
- D. Prescribe the level of detail needed to manage the work.

**Answer: D**

#### **NEW QUESTION 233**

- (Exam Topic 2)

An input to the Perform Integrated Change Control process is:

- A. expert judgment
- B. seller proposals
- C. the project charter
- D. the project management plan

**Answer: D**

#### **NEW QUESTION 235**

- (Exam Topic 2)

The component of the human resource management plan that includes ways in which team members can obtain certifications that support their ability to benefit the project is known as:

- A. recognition and rewards
- B. compliance
- C. staff acquisition
- D. training needs

**Answer: D**

#### **NEW QUESTION 239**

- (Exam Topic 2)

Which schedule method allows the project team to place buffers on the project schedule path to account for limited resources and project uncertainties?

- A. Critical path method
- B. Critical chain method
- C. Resource leveling
- D. Schedule network analysis

**Answer: B**

#### **NEW QUESTION 240**

- (Exam Topic 2)

Which tool or technique is required in order to determine the project budget?

- A. Cost of quality
- B. Historical relationships
- C. Project management software
- D. Forecasting

**Answer: B**

#### **NEW QUESTION 245**

- (Exam Topic 2)

The primary benefit of the Plan Schedule Management process is that it:

- A. provides guidance to identify time or schedule challenges within the project.
- B. tightly links processes to create a seamless project schedule.
- C. guides how the project schedule will be managed throughout the project.
- D. creates an overview of all activities broken down into manageable subsections.

**Answer: C**

#### **NEW QUESTION 249**

- (Exam Topic 2)

Which stakeholder approves a project's result?

- A. Customer
- B. Sponsor
- C. Seller
- D. Functional manager

**Answer: A**

#### NEW QUESTION 251

- (Exam Topic 2)

Which basic quality tool explains a change in the dependent variable in relationship to a change observed in the corresponding independent variable?

- A. Cause-and-effect diagram
- B. Histogram
- C. Control chart
- D. Scatter diagram

**Answer: D**

#### NEW QUESTION 255

- (Exam Topic 2)

Which item is a cost of conformance?


- A. Training
- B. Liabilities
- C. Lost business
- D. Scrap

**Answer: A**

#### NEW QUESTION 256

- (Exam Topic 2)

The following is a network diagram for a project.

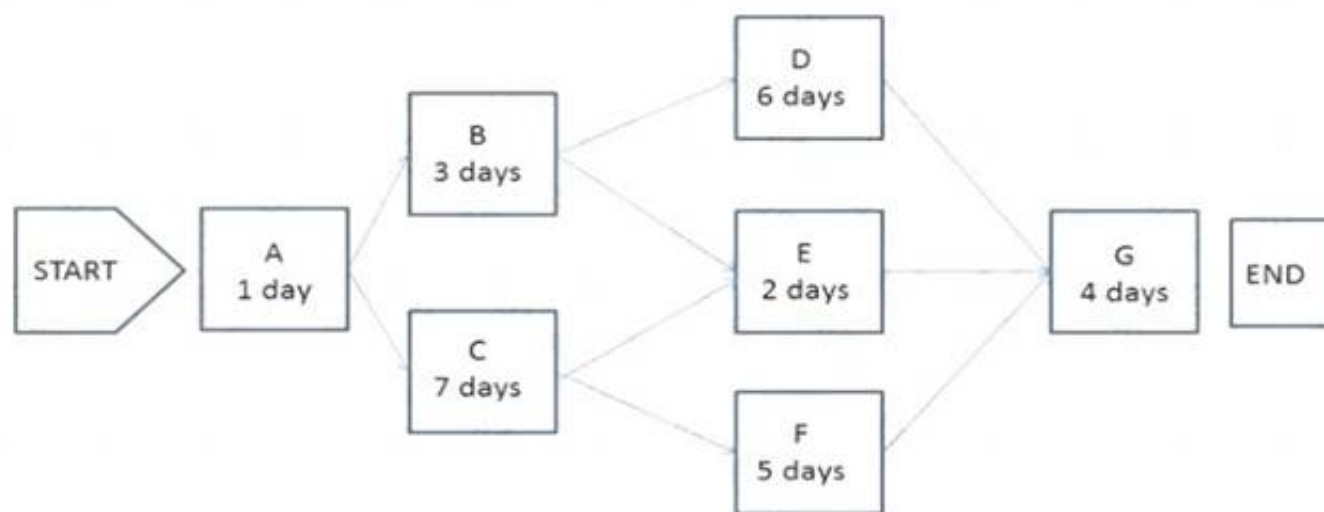

The shortest non-critical path for the project is how many days in duration?

- A. 10
- B. 12
- C. 14
- D. 16

**Answer: A**

#### NEW QUESTION 257

- (Exam Topic 2)

Analytical techniques are a tool and technique of which process in Project Procurement Management?

- A. Plan Procurement Management
- B. Control Procurements
- C. Conduct Procurements
- D. Close Procurements

**Answer: C**

#### NEW QUESTION 261

- (Exam Topic 1)

Which item is an output of Plan Quality Management and an input to Perform Quality Assurance?

- A. Organizational process updates
- B. Quality metrics
- C. Change requests
- D. Quality control measurements

**Answer: B**

#### NEW QUESTION 265

- (Exam Topic 1)

Which tool or technique is used in the Perform Integrated Change Control process?

- A. Decomposition
- B. Modeling techniques



- C. Resource optimization
- D. Meetings

**Answer:** D

#### NEW QUESTION 269

- (Exam Topic 1)

The process of identifying and documenting project roles, responsibilities, required skills, and reporting relationships and creating a staffing management plan is known as:

- A. Develop Project Team.
- B. Manage Project Team.
- C. Acquire Project Team.
- D. Plan Human Resource Management.

**Answer:** D

#### NEW QUESTION 270

- (Exam Topic 1)

Which tool or technique is used in the Plan Scope Management process?

- A. Document analysis
- B. Observations
- C. Product analysis
- D. Expert judgment

**Answer:** D

#### NEW QUESTION 275

- (Exam Topic 1)

The Monitoring and Controlling Process Group includes processes that:

- A. Establish the scope, objectives, and course of action of a project,
- B. Define a new project or a new phase of an existing project.
- C. Track, review, and regulate the progress and performance of a project.
- D. Complete the work defined in the project management plan.

**Answer:** C

#### NEW QUESTION 278

- (Exam Topic 1)

What is the schedule performance index (SPI) if the planned value (PV) is \$100, the actual cost (AC) is \$150, and the earned value (EV) is \$50?


- A. 0.50
- B. 0.67
- C. 1.50
- D. 2.00

**Answer:** A

#### NEW QUESTION 282

- (Exam Topic 2)

The following is a network diagram for a project.

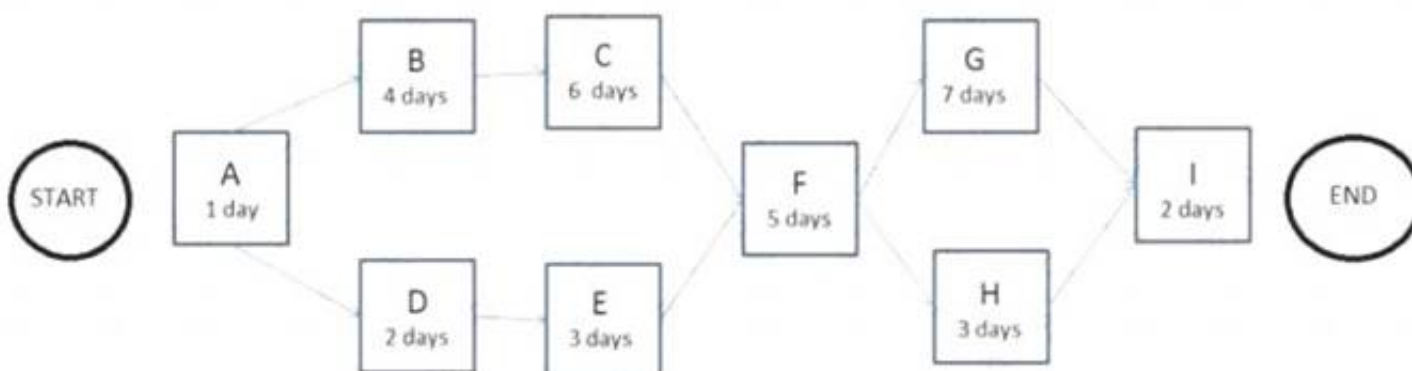

What is the critical path for the project?

- A. A-B-C-F-G-I
- B. A-B-C-F-H-I
- C. A-D-E-F-G-I
- D. A-D-E-F-H-I

**Answer:** A

#### NEW QUESTION 285

- (Exam Topic 1)

Which Control Quality tool is also known as an arrow diagram?

- A. Matrix diagram
- B. Affinity diagram
- C. Tree diagram
- D. Activity network diagram

**Answer:** D

**NEW QUESTION 286**

- (Exam Topic 1)

The iterative and interactive nature of the Process Groups creates the need for the processes in which Knowledge Area?

- A. Project Communications Management
- B. Project Integration Management
- C. Project Risk Management
- D. Project Scope Management

**Answer:** B

**NEW QUESTION 288**

- (Exam Topic 1)

Units of measure, level of precision, level of accuracy, control thresholds, and rules of performance measurement are examples of items that are established in the:

- A. Cost management plan.
- B. Work performance information.
- C. Quality management plan.
- D. Work breakdown structure.

**Answer:** A

**NEW QUESTION 293**

- (Exam Topic 1)

A tool or technique used in the Control Procurements process is:

- A. Expert judgment.
- B. Performance reporting.
- C. Bidder conferences.
- D. Reserve analysis.

**Answer:** B

**NEW QUESTION 296**

- (Exam Topic 1)

Which tool or technique is used to develop the human resource management plan?

- A. Ground rules
- B. Expert judgment
- C. Team-building activities
- D. Interpersonal skills

**Answer:** B

**NEW QUESTION 297**

- (Exam Topic 1)

Which item is an example of personnel assessment?

- A. Resource calendar
- B. Tight matrix
- C. Team-building activity
- D. Focus group

**Answer:** D

**NEW QUESTION 298**

- (Exam Topic 1)

Which risk management strategy seeks to eliminate the uncertainty associated with a particular upside risk by ensuring that the opportunity is realized?

- A. Enhance
- B. Share
- C. Exploit
- D. Accept

**Answer:** C

**NEW QUESTION 301**

- (Exam Topic 1)

Which tool or technique of the Define Activities process allows for work to exist at various levels of detail depending on where it is in the project life cycle?

- A. Historical relationships
- B. Dependency determination
- C. Bottom-up estimating
- D. Rolling wave planning

**Answer:** D

#### **NEW QUESTION 302**

- (Exam Topic 1)

Which Define Activities output extends the description of the activity by identifying the multiple components associated with each activity?

- A. Project document updates
- B. Activity list
- C. Activity attributes
- D. Project calendars

**Answer:** C

#### **NEW QUESTION 307**

- (Exam Topic 1)

Which process develops options and actions to enhance opportunities and reduce threats to project objectives?

- A. Identify Risks
- B. Control Risks
- C. Plan Risk Management
- D. Plan Risk Responses

**Answer:** D

#### **NEW QUESTION 308**

- (Exam Topic 1)

Organizational theory is a tool used in which Project Human Resource Management process?

- A. Manage Project Team
- B. Acquire Project Team
- C. Develop Project Team
- D. Plan Human Resource Management

**Answer:** D

#### **NEW QUESTION 311**

- (Exam Topic 1)

Which input to the Identify Stakeholders process provides information about internal or external parties related to the project?

- A. Procurement documents
- B. Communications plan
- C. Project charter
- D. Stakeholder register

**Answer:** C

#### **NEW QUESTION 316**

- (Exam Topic 1)

In the Plan Stakeholder Management process, expert judgment is used to:

- A. Provide information needed to plan appropriate ways to engage project stakeholders.
- B. Ensure comprehensive identification and listing of new stakeholders.
- C. Analyze the information needed to develop the project scope statement.
- D. Decide the level of engagement of the stakeholders at each required stage.

**Answer:** D

#### **NEW QUESTION 319**

- (Exam Topic 1)

Which Process Group and Knowledge Area include the Sequence Activities process?

- A. Executing Process Group and Project Time Management
- B. Executing Process Group and Project Cost Management
- C. Planning Process Group and Project Time Management
- D. Planning Process Group and Project Cost Management

**Answer:** C

**NEW QUESTION 320**

- (Exam Topic 1)

Which document describes the necessary information to determine if a project is worth the required investment?

- A. Cost baseline
- B. Service level agreement
- C. Memorandum of understanding
- D. Business case

**Answer:** D

**NEW QUESTION 324**

- (Exam Topic 1)

What are the Project Procurement Management processes?

- A. Conduct Procurements, Control Procurements, Integrate Procurements, and Close Procurements
- B. Estimate Procurements, Integrate Procurements, Control Procurements, and Validate Procurements
- C. Plan Procurement Management, Conduct Procurements, Control Procurements, and Close Procurements
- D. Plan Procurement Management, Perform Procurements, Control Procurements, and Validate Procurements

**Answer:** C

**NEW QUESTION 329**

- (Exam Topic 1)

Which input provides suppliers with a clear set of goals, requirements, and outcomes?

- A. Procurement statement of work
- B. Purchase order
- C. Source selection criteria
- D. Bidder conference

**Answer:** A

**NEW QUESTION 334**

- (Exam Topic 1)

Which input to the Plan Risk Management process provides information on high-level risks?

- A. Project charter
- B. Enterprise environmental factors
- C. Stakeholder register
- D. Organizational process assets

**Answer:** A

**NEW QUESTION 337**

- (Exam Topic 1)

A large portion of a projects budget is typically expended on the processes in which Process Group?

- A. Executing
- B. Planning
- C. Monitoring and Controlling
- D. Closing

**Answer:** B

**NEW QUESTION 342**

- (Exam Topic 1)

Which input to Collect Requirements is used to identify stakeholders who can provide information on requirements?

- A. Stakeholder register
- B. Scope management plan
- C. Stakeholder management plan
- D. Project charter

**Answer:** A

**NEW QUESTION 345**

- (Exam Topic 1)

Conditions that are not under the control of the project team that influence, direct, or constrain a project are called:

- A. Enterprise environmental factors
- B. Work performance reports
- C. Organizational process assets
- D. Context diagrams

**Answer:** A

**NEW QUESTION 350**

- (Exam Topic 1)

Which Knowledge Area involves identifying the people, groups, or organizations that may be impacted by or impact a project?

- A. Project Risk Management
- B. Project Human Resource Management
- C. Project Scope Management
- D. Project Stakeholder Management

**Answer:** D

**NEW QUESTION 355**

- (Exam Topic 1)

An input used in developing the communications management plan is:

- A. Communication models.
- B. Enterprise environmental factors.
- C. Organizational communications,
- D. Organizational cultures and styles.

**Answer:** B

**NEW QUESTION 358**

- (Exam Topic 1)

Which stakeholder classification model groups stakeholders based on their level of authority and their active involvement in the project?

- A. Power/influence grid
- B. Power/interest grid
- C. Influence/impact grid
- D. Salience model

**Answer:** A

**NEW QUESTION 360**

- (Exam Topic 1)

A risk response strategy in which the project team shifts the impact of a threat, together with ownership of the response, to a third party is called:

- A. mitigate
- B. accept
- C. transfer
- D. avoid

**Answer:** C

**NEW QUESTION 361**

- (Exam Topic 1)

Which quality management and control tool is useful in visualizing parent-to-child relationships in any decomposition hierarchy that uses a systematic set of rules that define a nesting relationship?

- A. Interrelationship digraphs
- B. Tree diagram
- C. Affinity diagram
- D. Network diagram

**Answer:** B

**NEW QUESTION 366**

- (Exam Topic 1)

The process of identifying and documenting relationships among the project activities is known as:

- A. Control Schedule.
- B. Sequence Activities.
- C. Define Activities.
- D. Develop Schedule.

**Answer:** B

**NEW QUESTION 371**

- (Exam Topic 1)

Which cost is associated with nonconformance?

- A. Liabilities
- B. Inspections
- C. Training
- D. Equipment

**Answer:** A

**NEW QUESTION 374**

- (Exam Topic 1)

Which process involves subdividing project deliverables and project work into smaller, more manageable portions?

- A. Develop Schedule
- B. Create WBS
- C. Estimate Activity Resources
- D. Define Scope

**Answer:** B

**NEW QUESTION 376**

- (Exam Topic 1)

Which basic quality tool is most useful when gathering attributes data in an inspection to identify defects?

- A. Control charts
- B. Pareto diagrams
- C. Ishikawa diagrams
- D. Checksheets

**Answer:** D

**NEW QUESTION 379**

- (Exam Topic 1)

Sensitivity analysis is typically displayed as a/an:

- A. Decision tree diagram.
- B. Tornado diagram.
- C. Pareto diagram.
- D. Ishikawa diagram.

**Answer:** B

**NEW QUESTION 384**

- (Exam Topic 1)

An example of a group decision-making technique is:

- A. Nominal group technique.
- B. Majority.
- C. Affinity diagram.
- D. Multi-criteria decision analysis.

**Answer:** B

**NEW QUESTION 388**

- (Exam Topic 6)

Which is the correct hierarchy in a project environment, from most to least Inclusive?

- A. Projects, portfolios, then programs
- B. Portfolios, programs, then projects
- C. Portfolios, projects, then programs
- D. Projects, programs, then portfolios

**Answer:** D

**NEW QUESTION 390**

- (Exam Topic 6)

What should a project manager use to determine how much money is needed to complete a project?

- A. Earned value management (EVM)
- B. Estimate at completion (EAC)
- C. Earned value analysis (EVA)
- D. Budget at completion (BAC)


**Answer:** B

**NEW QUESTION 391**

- (Exam Topic 6)

Match the influence with its corresponding category of influence.



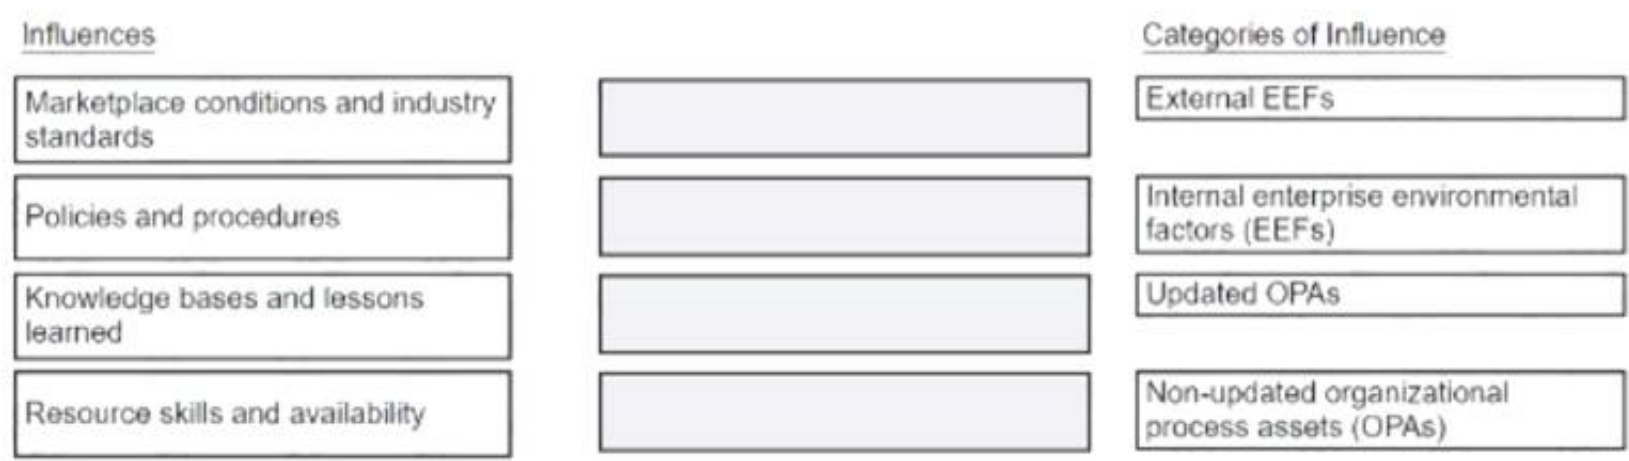

- A. Mastered
- B. Not Mastered

**Answer:** A

**Explanation:**



**NEW QUESTION 392**

- (Exam Topic 6)  
Why is tailoring in a project necessary?

- A. Requirements keep changing.
- B. An artifact must be produced.
- C. A tool or technique is required.
- D. Each project is unique.

**Answer:** D

**Explanation:**

Each project is unique, and the members of the project team should select the appropriate tools, techniques, inputs, and outputs from the PMBOK Guide.

**NEW QUESTION 394**

- (Exam Topic 6)  
A project team is discussing an upcoming planned product launch of a highly visible technologically advanced artificial intelligence tool. The team is debating the aspect of iterative and hybrid approaches. Which aspect of tailoring would this best represent?

- A. Life cycle approaches
- B. Resource availability
- C. Project dimensions
- D. Technology support

**Answer:** D

**NEW QUESTION 397**

- (Exam Topic 6)  
What is the best tool to calculate the critical path on a project?

- A. Critical chain method
- B. Graphical evaluation and review technique (GERT) diagram
- C. Gantt chart
- D. Project network diagram

**Answer:** C

**NEW QUESTION 401**

- (Exam Topic 6)  
An organizational structure that standardizes the project-related governance processes and facilitates the sharing of resources, methodologies, tools, and techniques is referred to as:

- A. Project Management Information System
- B. Project Management System
- C. Project Management Office
- D. Project Management Knowledge Area

**Answer:** C

**NEW QUESTION 406**

- (Exam Topic 6)

A project manager is reviewing the change requests for project documents, deliverables, and the project plan. In which project management process does this review belong?

- A. Monitor and Control Project Work
- B. Direct and Manage Project Work
- C. Close Project or Phase
- D. Perform Integrated Change Control

**Answer:** D

**NEW QUESTION 407**

- (Exam Topic 5)

The correct equation for schedule variance (SV) is earned value:

- A. minus planned value [EV - PV].
- B. minus actual cost [EV - AC].
- C. divided by planned value [EV/PV],
- D. divided by actual cost [EV/AC].

**Answer:** A

**NEW QUESTION 410**

- (Exam Topic 5)

Using the three-point estimating technique, if the most likely duration is four months, the optimistic duration is two months, and the pessimistic duration is one year, how many months is the expected activity duration?

- A. Two
- B. Four
- C. Five
- D. Twelve

**Answer:** C

**NEW QUESTION 411**

- (Exam Topic 5)

Which of the following change requests can bring expected future performance of the project work in line with the project management plan?

- A. Corrective action
- B. Defect repair
- C. Preventative action
- D. Probable action

**Answer:** A

**NEW QUESTION 412**

- (Exam Topic 5)

Which type of diagram includes groups of information and shows relationships between factors, causes, and objectives?

- A. Affinity
- B. Scatter
- C. Fishbone
- D. Matrix

**Answer:** D

**NEW QUESTION 415**

- (Exam Topic 5)

Which Control Scope input is compared to actual results to determine if corrective action is required for the project?

- A. Scope baseline
- B. Scope management plan
- C. Change management plan
- D. Cost baseline


**Answer:** A



**NEW QUESTION 418**

- (Exam Topic 5)

The diagram below is an example of a:

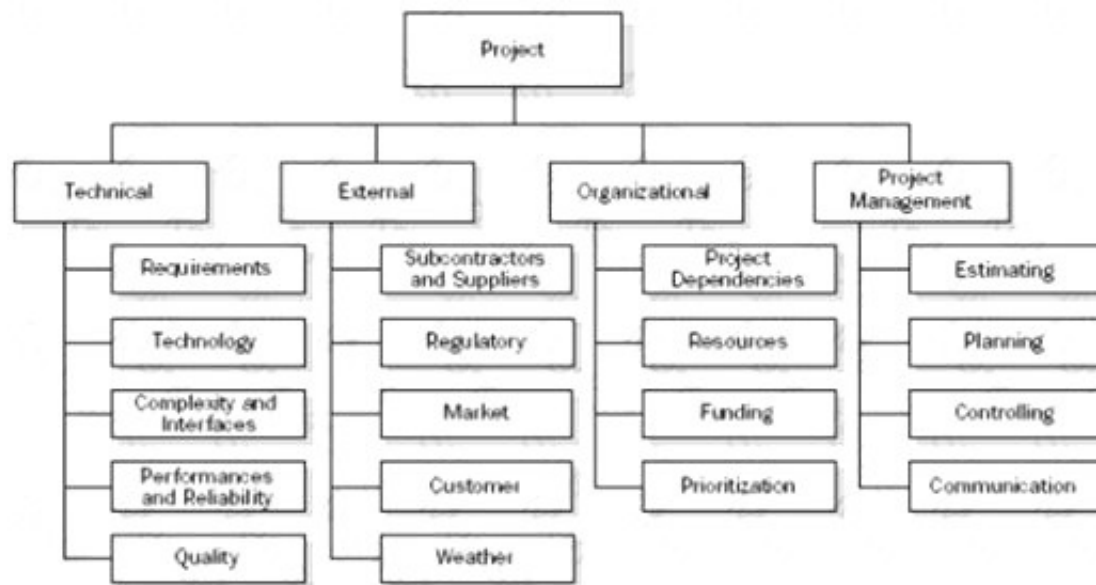

- A. Risk breakdown structure (RBS).
- B. Project team.
- C. SWOT Analysis.
- D. Work breakdown structure (WBS).

**Answer: A**

**NEW QUESTION 420**

- (Exam Topic 5)

Which input will be used when tasked with developing the human resource plan?

- A. Project management plan
- B. Activity resource requirements
- C. Resource calendar
- D. Project staff assignments

**Answer: B**

**NEW QUESTION 425**

- (Exam Topic 5)

The risk shared between the buyer and seller is determined by the:

- A. assumption log.
- B. quality checklist.
- C. risk register.
- D. contract type.

**Answer: D**

**NEW QUESTION 426**

- (Exam Topic 5)

The process to ensure that appropriate quality standards and operational definitions are used is:

- A. Plan Quality.
- B. Perform Quality Assurance.
- C. Perform Quality Control.
- D. Total Quality Management.

**Answer: B**

**NEW QUESTION 427**

- (Exam Topic 5)

Expected monetary value (EMV) is computed by which equation?

- A. Value of each possible outcome multiplied by probability of occurrence
- B. Value of each possible outcome multiplied by probability of non-occurrence
- C. Multiplying the value of each possible outcome by the probability of occurrence and adding the products together
- D. Multiplying the value of each possible outcome by the probability of non-occurrence and adding the products together

**Answer: C**

**NEW QUESTION 430**

- (Exam Topic 5)

Which of the following is an estimating technique that uses the values of parameters from previous similar projects for estimating the same parameter or measure for a current project?

- A. Reserve analysis
- B. Three-point estimating
- C. Parametric estimating
- D. Analogous estimating

**Answer:** D

**NEW QUESTION 435**

- (Exam Topic 5)

Which of the following is a statistical concept that calculates the average outcome when the future includes scenarios that may or may not happen?

- A. Sensitivity analysis
- B. Three-point estimate
- C. Modeling and simulation
- D. Expected monetary value analysis

**Answer:** D

**NEW QUESTION 439**

- (Exam Topic 5)

At which stage of team development do members begin to work together, adjust work habits, and trust each other?

- A. Forming
- B. Storming
- C. Norming
- D. Performing

**Answer:** C

**NEW QUESTION 443**

- (Exam Topic 5)

Projects are separated into phases or subprojects; these phases include:

- A. feasibility study, concept development, design, and prototype.
- B. initiate, plan, execute, and monitor.
- C. Develop Charter, Define Activities, Manage Stakeholder Expectations, and Report Performance.
- D. Identify Stakeholders, develop concept, build, and test.

**Answer:** A

**NEW QUESTION 447**

- (Exam Topic 5)

Who determines which dependencies are mandatory during the Sequence Activities process?

- A. Project manager
- B. External stakeholders
- C. Internal stakeholders
- D. Project team

**Answer:** D

**NEW QUESTION 448**

- (Exam Topic 5)

The process of identifying specific actions to be performed to produce project deliverables is:

- A. Define Activities.
- B. Create WBS.
- C. Define Scope.
- D. Develop Schedule.

**Answer:** A

**NEW QUESTION 451**

- (Exam Topic 5)

A project manager has created an issue log to document issues communicated by project team members during weekly team meetings. This is an input of:

- A. Manage Stakeholder Expectations.
- B. Monitor and Control Risks.
- C. Plan Risk Management.
- D. Report Performance.

**Answer:** A

**NEW QUESTION 454**

- (Exam Topic 5)

The project has a current cost performance index of 0.80. Assuming this performance will continue, the new estimate at completion is \$1000. What was the original budget at completion for the project?

- A. \$800
- B. \$1000
- C. \$1250
- D. \$1800

**Answer:** A

#### **NEW QUESTION 458**

- (Exam Topic 5)

Which type of contract is a hybrid of both a cost-reimbursable and a fixed-price contract?

- A. Cost Plus Award Fee Contract (CPAF)
- B. Firm-Fixed -Price Contract (FFP)
- C. Time and Material Contract (T&M)
- D. Cost Plus Incentive Fee Contract (CPIF)

**Answer:** C

#### **NEW QUESTION 463**

- (Exam Topic 5)

A tool and technique used during the Define Scope process is:

- A. facilitated workshops.
- B. observations.
- C. questionnaires and surveys.
- D. group creativity techniques.

**Answer:** A

#### **NEW QUESTION 465**

- (Exam Topic 5)

After Define Activities and Sequence Activities, the next process is:

- A. Estimate Activity Resources.
- B. Estimate Activity Durations,
- C. Develop Schedule.
- D. Control Schedule.

**Answer:** A

#### **NEW QUESTION 468**

- (Exam Topic 5)

Who is responsible for initiating a project?

- A. Project sponsor
- B. Project manager
- C. Program manager
- D. Project management office (PMO)

**Answer:** A

#### **NEW QUESTION 473**

- (Exam Topic 5)

Which statement is true about the project management body of knowledge?

- A. Recognized by every project manager
- B. Constantly evolving
- C. The sum of all knowledge related to project management
- D. A sum of knowledge that should be applied on every project

**Answer:** B

#### **NEW QUESTION 474**

- (Exam Topic 5)

The contract in which the seller is reimbursed for all allowable costs for performing the contract work and then receives a fee based upon achieving certain performance objectives is called a:

- A. Cost Plus Incentive Fee Contract (CPIF).
- B. Cost Plus Fixed Fee Contract (CPFF).
- C. Fixed Price Incentive Fee Contract (FPIF).
- D. Time and Material Contract (T&M).

**Answer:** A

#### NEW QUESTION 475

- (Exam Topic 5)

Which is one of the determining factors used to calculate CPI?

- A. EV
- B. SPI
- C. PV
- D. ETC

**Answer:** A

#### NEW QUESTION 477

- (Exam Topic 5)

Risk exists the moment that a project is:

- A. planned.
- B. conceived.
- C. chartered.
- D. executed.

**Answer:** B

#### NEW QUESTION 478

- (Exam Topic 5)

The project budget is set at \$150,000. The project duration is planned to be one year. At the completion of Week 16 of the project, the following information is collected: Actual cost = \$50,000, Plan cost = \$45,000, Earned value = \$40,000. What is the cost performance index?

- A. 0.8
- B. 0.89
- C. 1.13
- D. 1.25

**Answer:** A

#### NEW QUESTION 480

- (Exam Topic 5)

Which statement correctly describes the value of a business case?

- A. It provides the necessary information to determine if a project is worth the required investment.
- B. It provides for alternative dispute resolution procedures in event of contract default.
- C. It offers one of several alternative scenarios which assist in performing qualitative risk analysis.
- D. It is used to help a project manager understand the scope of commercial advantages.

**Answer:** A

#### NEW QUESTION 484

- (Exam Topic 5)

Which quality control technique illustrates the 80/20 principle?

- A. Ishikawa diagram
- B. Control chart
- C. Run chart
- D. Pareto chart

**Answer:** D

#### NEW QUESTION 489

- (Exam Topic 5)

An input to the Collect Requirements process is the:

- A. stakeholder register.
- B. project management plan.
- C. project scope statement.
- D. requirements management plan.

**Answer:** A

#### NEW QUESTION 493

- (Exam Topic 5)

The three processes of Project Cost Management are:

- A. Estimate Costs, Control Schedule, and Control Costs.
- B. Estimate Costs, Determine Budget, and Estimate Activity Resources.
- C. Determine Budget, Control Schedule, and Estimate Activity Resources.
- D. Estimate Costs, Determine Budget, and Control Costs.

**Answer:**

D

**NEW QUESTION 494**

- (Exam Topic 5)

How should a stakeholder who is classified as high power and low interest be grouped in a power/interest grid during stakeholder analysis?

- A. Keep satisfied
- B. Keep informed
- C. Manage closely
- D. Monitor

**Answer: A**

**NEW QUESTION 496**

- (Exam Topic 5)

The process improvement plan details the steps for analyzing processes to identify activities which enhance their:

- A. quality.
- B. value.
- C. technical performance.
- D. status.

**Answer: B**

**NEW QUESTION 499**

- (Exam Topic 5)

In which type of contract are the performance targets established at the onset and the final contract price determined after completion of all work based on the sellers performance?

- A. Firm-Fixed-Price (FFP)
- B. Fixed Price with Economic Price Adjustments (FP-EPA)
- C. Fixed-Price-Incentive-Fee (FPIF)
- D. Cost Plus Fixed Fee (CPFF)

**Answer: C**

**NEW QUESTION 503**

- (Exam Topic 4)

Which of the following helps to ensure that each requirement adds business value by linking it to the business and project objectives?

- A. Requirements traceability matrix
- B. Work breakdown structure (WBS) dictionary
- C. Requirements management plan
- D. Requirements documentation

**Answer: A**

**NEW QUESTION 507**

- (Exam Topic 4)

In a construction project schedule, what is the logical relationship between the delivery of the concrete materials and the pouring of concrete?

- A. Start-to-start (SS)
- B. Start-to-finish (SF)
- C. Finish-to-finish (FF)
- D. Finish-to-start (FS)

**Answer: D**

**NEW QUESTION 511**

- (Exam Topic 4)

What is the schedule performance index (SPI) using the following data? BAC = \$100,000 PV = \$50,000 AC = \$80,000 EV = \$40,000

- A. 1
- B. 0.4
- C. 0.5
- D. 0.8

**Answer: D**

**NEW QUESTION 512**

- (Exam Topic 4)

Quality metrics are an output of which process?

- A. Plan Quality
- B. Perform Quality Control
- C. Perform Quality Assurance

D. Perform Qualitative Risk Analysis

**Answer:** A

**NEW QUESTION 514**

- (Exam Topic 4)

What risk technique is used to quantify the probability and impact of risks on project objectives?

- A. Expert judgment
- B. Risk registry
- C. Risk response planning
- D. Interviewing

**Answer:** D

**NEW QUESTION 515**

- (Exam Topic 4)

Which of the following is the primary output of the Identify Risks process?

- A. Risk management plan
- B. Risk register
- C. Change requests
- D. Risk response plan

**Answer:** B

**NEW QUESTION 519**

- (Exam Topic 4)

What does a CPI value greater than 1.0 indicate?

- A. Cost right at the estimated value
- B. Cost under the estimated value
- C. Cost right at the actual value
- D. Cost over the estimated value

**Answer:** B

**NEW QUESTION 521**

- (Exam Topic 4)

Which activity involves ensuring that the composition of a projects configuration items is correct?

- A. Configuration Identification
- B. Configuration Status Accounting
- C. Configuration Verification and Audit
- D. Configuration Quality Assurance

**Answer:** C

**NEW QUESTION 524**

- (Exam Topic 4)

Which written document helps monitor who is responsible for resolving specific problems and concerns by a target date?

- A. Project Plan
- B. Responsibility Matrix
- C. Issue Log
- D. Scope Document

**Answer:** C

**NEW QUESTION 526**

- (Exam Topic 4)

Which of the following processes audits the quality requirements and the results from quality control measures to ensure appropriate quality standards and operational definitions are used?

- A. Perform Quality Control
- B. Quality Metrics
- C. Perform Quality Assurance
- D. Plan Quality

**Answer:** C

**NEW QUESTION 528**

- (Exam Topic 4)

Which standard has interrelationships to other project management disciplines such as program management and portfolio management?

- A. Program Management Body of Knowledge Guide
- B. The Standard for Program Management
- C. Organizational Project Management Maturity Model (OPM3\$)
- D. Guide to the Project Management Body of Knowledge (PMBOK®)

**Answer:** D

**NEW QUESTION 530**

- (Exam Topic 4)

Documented identification of a flaw in a project component together with a recommendation is termed a:

- A. corrective action.
- B. preventive action.
- C. non-conformance report,
- D. defect repair.

**Answer:** D

**NEW QUESTION 532**

- (Exam Topic 4)

A tool or technique in Perform Quality Control that a project manager would use is:

- A. quality audits.
- B. process analysis.
- C. benchmarking.
- D. inspection.

**Answer:** D

**NEW QUESTION 537**

- (Exam Topic 4)

Who provides the inputs for the original estimates of activity durations for tasks on the project plan?

- A. Project sponsor
- B. Project manager
- C. Person responsible for project scheduling
- D. Person who is most familiar with the task

**Answer:** D

**NEW QUESTION 540**

- (Exam Topic 4)

In the Develop Project Team process, which of the following is identified as a critical factor for a project's success?

- A. Team meetings
- B. Subcontracting teams
- C. Virtual teams
- D. Teamwork

**Answer:** D

**NEW QUESTION 543**

- (Exam Topic 4)

What is a tool to improve team performance?

- A. Staffing plan
- B. External feedback
- C. Performance reports
- D. Co-location

**Answer:** D

**NEW QUESTION 548**

- (Exam Topic 4)

Which of the following is an output of the Distribute Information process?

- A. Project calendar
- B. Communications management plan
- C. Organizational process assets updates
- D. Project document updates

**Answer:** C

**NEW QUESTION 550**

- (Exam Topic 4)



Which provides the basic framework for managing a project?

- A. Project life cycle
- B. Work breakdown structure (WBS)
- C. Enterprise environmental factors
- D. Project initiation

**Answer:** A

**NEW QUESTION 551**

- (Exam Topic 4)

During which process would stakeholders provide formal acceptance of the completed project scope?

- A. Perform Quality Control
- B. Verify Scope
- C. Control Scope
- D. Develop Schedule

**Answer:** B

**NEW QUESTION 553**

- (Exam Topic 4)

Which of the following Process Groups covers all nine Project Management Knowledge Areas?

- A. Executing
- B. Monitoring and Controlling
- C. Planning
- D. Initiating

**Answer:** C

**NEW QUESTION 554**

- (Exam Topic 4)

When calculating the cost of quality (COQ) for a product or service, money spent for cost of conformance would include the areas of:

- A. training, testing, and warranty work.
- B. equipment, rework, and scrap.
- C. training, document processes, and inspections.
- D. inspections, rework, and warranty work.

**Answer:** C

**NEW QUESTION 559**

- (Exam Topic 4)

Which is an output from Distribute Information?

- A. Earned value analysis
- B. Trend analysis
- C. Project records
- D. Performance reviews

**Answer:** C

**NEW QUESTION 560**

- (Exam Topic 4)

The risk management team of a software project has decided that due to the lack of adequate talent in the company, development of a specific part of the system is under high risk, so the team has decided to outsource it. This is an example of which risk response?

- A. Transfer
- B. Share
- C. Avoid
- D. Accept

**Answer:** A

**NEW QUESTION 561**

- (Exam Topic 4)

The precedence diagramming method (PDM) is also known as:

- A. Arrow Diagram.
- B. Critical Path Methodology (CPM).
- C. Activity-On-Node (AON).
- D. schedule network diagram.

**Answer:** C



**NEW QUESTION 564**

- (Exam Topic 4)

Which of the following is an output from Control Scope?

- A. Change requests
- B. Variance analysis
- C. Accepted deliverables
- D. Requirements documentation

**Answer:** A

**NEW QUESTION 569**

- (Exam Topic 4)

A method to manage stakeholder expectations in the scope statement is to clearly:

- A. state the guiding principles of the organization.
- B. identify alternatives to generate different approaches.
- C. state what is out of scope.
- D. outline the results of the Delphi technique.

**Answer:** C

**NEW QUESTION 574**

- (Exam Topic 4)

In which process is a project manager identified and given the authority to apply resources to project activities?

- A. Acquire Project Team
- B. Develop Project Management Plan
- C. Manage Project Execution
- D. Develop Project Charter

**Answer:** D

**NEW QUESTION 579**

- (Exam Topic 4)

The definition of operations is a/an:

- A. organizational function performing the temporary execution of activities that produce the same product or provide repetitive service.
- B. temporary endeavor undertaken to create a unique product, service, or result.
- C. organization that provides oversight for an administrative area.
- D. organizational function performing the ongoing execution of activities that produce the same product or provide repetitive service.

**Answer:** D

**NEW QUESTION 580**

- (Exam Topic 4)

Which of the following outputs from the Control Schedule process aids in the communication of schedule variance (SV), schedule performance index (SPI), or any performance status to stakeholders?

- A. Performance organizations
- B. Schedule baselines
- C. Work performance measurements
- D. Change requests

**Answer:** C

**NEW QUESTION 582**

- (Exam Topic 4)

Which characteristic do projects and operational work share in common?

- A. Performed by systems
- B. Constrained by limited resources
- C. Repetitiveness
- D. Uniqueness

**Answer:** B

**NEW QUESTION 587**

- (Exam Topic 4)

The Project Management Process Group in which performance is observed and measured regularly from project initiation through completion is:

- A. Executing.
- B. Initiating,
- C. Monitoring and Controlling.
- D. Planning.

**Answer:**

C

**NEW QUESTION 589**

- (Exam Topic 4)

The progressive detailing of the project management plan is called:

- A. expert judgment.
- B. rolling wave planning.
- C. work performance information.
- D. specification.

**Answer: B**

**NEW QUESTION 594**

- (Exam Topic 4)

Which tool and technique is used in Conduct Procurements?

- A. Teaming agreements
- B. Expert judgment
- C. Bidder conferences
- D. Contract types

**Answer: C**

**NEW QUESTION 596**

- (Exam Topic 4)

What is the responsibility of the project manager and the functional manager respectively?

- A. Oversight for an administrative area; a facet of the core business
- B. Achieving the project objectives; providing management oversight for an administrative area
- C. A facet of the core business; achieving the project objectives
- D. Both are responsible for achieving the project objectives.

**Answer: B**

**NEW QUESTION 599**

- (Exam Topic 4)

Another name for an Ishikawa diagram is:

- A. cause and effect diagram.
- B. control chart.
- C. flowchart.
- D. histogram.

**Answer: A**

**NEW QUESTION 602**

- (Exam Topic 4)

Which is used to solicit proposals from prospective sellers?

- A. Procurement statement of work
- B. Resource calendars
- C. Procurement document
- D. Independent estimates

**Answer: C**

**NEW QUESTION 605**

- (Exam Topic 4)

Which is a communication method used in the Report Performance process?

- A. Expert judgment
- B. Project management methodology
- C. Stakeholder analysis
- D. Status review meetings

**Answer: D**

**NEW QUESTION 609**

- (Exam Topic 4)

Which Process Group contains those processes performed to define a new project?

- A. Initiating
- B. Planning
- C. Executing
- D. Closing

**Answer:** A

**NEW QUESTION 610**

- (Exam Topic 4)

Testing falls into which of the following categories of cost of quality?

- A. Internal failure costs
- B. Prevention costs
- C. Appraisal costs
- D. External failure costs

**Answer:** C

**NEW QUESTION 612**

- (Exam Topic 4)

What is a deliverable-oriented, hierarchical decomposition of the work to be executed to accomplish the project objectives and create the required deliverables?

- A. Organizational breakdown structure (OBS)
- B. Work performance information
- C. Work package
- D. Work breakdown structure (WBS)

**Answer:** D

**NEW QUESTION 615**

- (Exam Topic 4)

Which of the following statements is true regarding project and product lifecycles?

- A. A single product lifecycle may consist of multiple project lifecycles.
- B. A product lifecycle is always shorter than the project lifecycle.
- C. A single product lifecycle can only have one project lifecycle.
- D. A single project lifecycle may consist of multiple product lifecycles.

**Answer:** A

**NEW QUESTION 616**

- (Exam Topic 4)

Which of the following factors is lowest at the start of the project?

- A. Cost of changes
- B. Stakeholder influences
- C. Risk
- D. Uncertainty

**Answer:** A

**NEW QUESTION 618**

- (Exam Topic 4)

The process of monitoring the status of the project to update project progress and manage changes to the schedule baseline is:

- A. Control Schedule.
- B. Quality Control.
- C. Perform Integrated Change Control.
- D. Develop Schedule.

**Answer:** A

**NEW QUESTION 623**

- (Exam Topic 6)

Which tool should a project manager consider to deal with multiple sources of risk?

- A. An updated risk register
- B. Risk breakdown structure
- C. Issue log
- D. Stakeholder register

**Answer:** B

**NEW QUESTION 627**

- (Exam Topic 6)

A project manager has just completed several brainstorming sessions and has gathered the data to show commonality and differences in one single place. What technique was followed?

- A. Collective decision making
- B. Multicriteria decision analysis

- C. Mind mapping
- D. Affinity diagram

**Answer:** C

**NEW QUESTION 629**

- (Exam Topic 6)

Perform Quantitative Risk Analysis focuses on:

- A. compiling a list of known risks and preparing responses to them.
- B. assessing the probability of occurrence and Impact for every risk in the risk register.
- C. evaluating the contingency and management reserves required for the project.
- D. analyzing numerically the impact of individual risks on the overall project's time and cost objectives.

**Answer:** D

**NEW QUESTION 631**

- (Exam Topic 6)

A project manager is working in an environment where requirements are not very clear and may change during the project. In addition, the project has several stakeholders and is technically complex.

Which strategies should the project manager take into account for risk management in this environment?

- A. Occasionally identify, evaluate, and classify risks.
- B. Review requirements and cross-functional project teams.
- C. Include contingency reserves and update the project management plan frequently.
- D. Frequently review incremental work products and update the requirements for proper prioritization.

**Answer:** D

**NEW QUESTION 636**

- (Exam Topic 6)

Which of the following is used as an input to prepare a cost management plan?

- A. Expert judgment
- B. Lessons learned
- C. Cost estimates
- D. Project management plan

**Answer:** D

**NEW QUESTION 641**

- (Exam Topic 6)

Which of the following sets are inputs to the Collect Requirements process?

- A. Project charter and requirements documentation
- B. Project charter and business documents
- C. Project charter and stakeholder requirements
- D. Business documents and requirements traceability matrix

**Answer:** B

**NEW QUESTION 642**

- (Exam Topic 6)

The Agile principle "welcome changing requirement, even late in development" relates to which agile manifesto?

- A. Working software over comprehensive documentation
- B. Individuals and interactions over processes and tools
- C. Customer collaboration over contract negotiation
- D. Responding to change over following a plan

**Answer:** D

**NEW QUESTION 646**

- (Exam Topic 6)

Once the make-or-buy analysis is completed, which document defines the project delivery method?

- A. Procurement statement of work (SOW)
- B. Procurement strategy
- C. Terms of reference
- D. Change request

**Answer:** B

**NEW QUESTION 651**

- (Exam Topic 6)

It you established a contingency reserve including time, money, and resources, how are you handling risk?

- A. Accepting
- B. Transferring
- C. Avoiding
- D. Mitigating

**Answer:** A

**NEW QUESTION 652**

- (Exam Topic 6)

A new project has been set. Four main stakeholders besides the project manager and four other team members have been identified. How many communication channels are available?

- A. 8
- B. 18
- C. 36
- D. 40

**Answer:** C

**NEW QUESTION 657**

- (Exam Topic 6)

A team receives four different requests from separate stakeholders related to one application Match each requirement with its corresponding type of change request.

Requirement		Type of Change Request
Add new functionality to the application		Update
Recover from a three-day delay		Defect repair
Reduce login time due to a corrupt login script		Preventive action
Install alarms to alert for non-conformances		Corrective action

- A. Mastered
- B. Not Mastered

**Answer:** A

**Explanation:**

Requirement		Type of Change Request
Add new functionality to the application	Add new functionality to the application	Update
Recover from a three-day delay	Install alarms to alert for non-conformances	Defect repair
Reduce login time due to a corrupt login script	Recover from a three-day delay	Preventive action
Install alarms to alert for non-conformances	Reduce login time due to a corrupt login script	Corrective action

**NEW QUESTION 661**

- (Exam Topic 6)

Match the project life cycle type with its corresponding definition.

Project Life Cycle Type		Definition
Adaptive		The detailed scope is defined and approved before the start of an iteration.
Incremental		The project scope is determined early in the project life cycle, but time and cost estimates are modified as an understanding of the product increases.
Predictive		The project's scope, time, and cost are determined in the early phases of the life cycle.
Iterative		The deliverable is produced through a series of iterations that successively add functionality within a predetermined timeframe.

- A. Mastered  
B. Not Mastered

**Answer:** A

**Explanation:**

ADAPTATIVE ITERATIVE PREDICTIVE  
INCREMENTAL

#### NEW QUESTION 665

- (Exam Topic 6)

A project manager Is in the process of working with stakeholders to meet their needs and expectations, and identifying and fostering communication and involvement. Which process does this typically represent?

- A. Monitor Stakeholder Engagement  
B. Monitor Communications  
C. Manage Communications  
D. Manage Stakeholder Engagement

**Answer:** D

#### NEW QUESTION 667

- (Exam Topic 6)

What is the discipline that focuses on the interdependences between projects to determine the optimal approach for managing them?

- A. Project Management  
B. Program Management  
C. Portfolio Management  
D. Operations Management

**Answer:** A

#### NEW QUESTION 669

- (Exam Topic 6)

A functional manager is delegating a key project to a project team without a project manager. Which communication method will be most effective?

- A. Interactive  
B. Push  
C. Verbal  
D. Oral

**Answer:** A

#### NEW QUESTION 670

- (Exam Topic 6)

The project manager is working in the processes of Project Resource Management. Which process is the project manager developing if they are using parametric estimation?

- A. Plan Resource Management  
B. Estimate Activity Resources  
C. Estimate Costs



D. Acquire Resources

**Answer:** B

**NEW QUESTION 673**

- (Exam Topic 6)

A project manager is formalizing acceptance of the completed project deliverables. What is an input to this process?

- A. Verified deliverables
- B. Validated deliverables
- C. Accepted deliverables
- D. Completed change requests

**Answer:** A

**NEW QUESTION 675**

- (Exam Topic 6)

What organizational asset can influence the Plan Risk Management process?

- A. Corporate policies and procedures for social media, ethics, and security
- B. Organizational risk policy
- C. Stakeholder register templates and instructions
- D. Organizational communication requirements

**Answer:** C

**NEW QUESTION 678**

- (Exam Topic 6)

A firm contracted an event management company to conduct the annual sales day event. The agreement states that the event management company will charge the firm for the actuals and receive 8% of the total cost. What type of contract is this?

- A. Time and material (T&M)
- B. Fixed price incentive fee (FPIF)
- C. Cost plus fixed fee (CPFF)
- D. Cost plus award fee (CPAF)

**Answer:** C

**NEW QUESTION 681**

- (Exam Topic 6)

What important leadership quality/qualities should project managers possess?

- A. Skills and behaviors related to specific domains of project management
- B. Skills and behaviors needed to guide a team and help an organization reach its goals
- C. Industry expertise that helps to better deliver business outcomes
- D. Industry and organizational expertise that enhances performance

**Answer:** C

**NEW QUESTION 684**

- (Exam Topic 6)

What tool should a project manager use to efficiently manage project resources?

- A. List of project resources
- B. Resource breakdown structure
- C. Resources detailed in the project scope
- D. Resource requirements

**Answer:** C

**NEW QUESTION 686**

- (Exam Topic 6)

How can a project manager evaluate project team development?

- A. Produce team performance assessments.
- B. Hold weekly meetings to engage every member
- C. Complete a personal skill assessment on each team member
- D. Provide recognition awards to team members

**Answer:** A

**NEW QUESTION 688**

- (Exam Topic 6)

Which are inputs for the Plan Quality Management process?

- A. Quality metrics, project documents, and financial performance
- B. Quality management plan, project documents, and quality metrics
- C. Project management plan, project documents, and organizational process assets
- D. Project management plan, quality metric
- E. and project documents

**Answer:** C

#### NEW QUESTION 689

- (Exam Topic 6)

Which tasks should a project manager perform in order to manage the project schedule effectively?

- A. Plan Schedule Management, Define Activities, Sequence Activities, Estimate Activity Durations, Define Quality of Activities
- B. Develop Schedule
- C. Plan Schedule Management
- D. Define Activities, Sequence Activities, Estimate Activity Durations, Develop Schedule
- E. Control Schedule
- F. Plan Schedule Management
- G. Define Activities, Sequence Activities, Estimate Activity Durations, Estimate Cost of Activities
- H. Develop Schedule
- I. Define Activities
- J. Sequence Activities, Estimate Activity Duration
- K. Define Quality of Activities, Estimate Cost of Activities, Develop Schedule

**Answer:** B

#### NEW QUESTION 694

- (Exam Topic 6)

Which of the following lists represents the outputs of the Monitor Communications process?

- A. Project communications, project management plan updates, project documents updates, and organizational process assets updates
- B. Work performance information, change requests, project management plan updates, and project documents updates
- C. Communications management plan, project management plan updates, work performance report, and project documents update
- D. Stakeholder engagement plan, change requests, project management plan updates, and project documents updates

**Answer:** B

#### NEW QUESTION 698

- (Exam Topic 6)

Which of the following is an example of tacit knowledge?

- A. Risk register
- B. Project requirements
- C. Expert judgment
- D. Make-or-buy analysis

**Answer:** C

#### NEW QUESTION 700

- (Exam Topic 6)

A project manager needs to demonstrate that the project meets quality standards and success criteria. For that reason, the project manager is defining the quality objectives of the project, the quality tools that will be used, and quality metrics for the project deliverables.

Which process is the project manager executing?

- A. Manage Quality
- B. Plan Quality Management
- C. Control Quality
- D. Plan Scope Management

**Answer:** B

#### NEW QUESTION 701

- (Exam Topic 6)

During the execution phase of a project a defect is found. The project manager takes responsibility and with the correct documentation, begins the task necessary to repair the defect. What process was applied?

- A. Change request
- B. Risk response
- C. Risk management plan
- D. Lessons learned

**Answer:** A

#### NEW QUESTION 706

- (Exam Topic 6)

Which of the following is an example of an organizational system that is arranged based on the job being performed?



- A. Simple
- B. Multi-divisional
- C. Functional
- D. Project-oriented

**Answer:** C

**NEW QUESTION 710**

- (Exam Topic 6)

When should Project Risk Management be conducted?

- A. Project Planning
- B. Monitoring and Controlling
- C. Quality Planning
- D. Throughout the project lifecycle

**Answer:** C

**NEW QUESTION 714**

- (Exam Topic 6)

How can a project manager determine if the project activities comply with organizational and project policies, processes, and procedures?

- A. Look at the quality metrics.
- B. Validate the scope.
- C. Review the quality checklist.
- D. Conduct a quality audit.

**Answer:** D

**NEW QUESTION 717**

- (Exam Topic 6)

A project manager needs to tailor the Project Cost Management process. Which considerations should the project manager apply?

- A. Diversity background
- B. Stakeholder's relationships
- C. Technical expertise
- D. Knowledge management

**Answer:** D

**NEW QUESTION 720**

- (Exam Topic 6)

Which is an example of leveraging evolving trends and emerging practices in Project Integration Management?

- A. Hybrid methodologies
- B. Risk register updates
- C. Outsourced project resources
- D. Reliance on lessons learned documents

**Answer:** A

**NEW QUESTION 724**

- (Exam Topic 6)

Which of the following can a project manager use to represent defined team member roles in a group of tasks?

- A. Work breakdown structure (WBS)
- B. Responsibility assignment matrix (RAM)
- C. Organizational breakdown structure (OBS)
- D. Resource breakdown structure (RBS)

**Answer:** B

**NEW QUESTION 725**

- (Exam Topic 6)

Which components of the project management plan are inputs used when creating the stakeholder engagement plan?

- A. Risk, resource, and communications management plans
- B. Scope, quality, and resource management plans
- C. Procurement, integration, and risk management plans
- D. Communications, schedule, and cost management plans

**Answer:** A

**NEW QUESTION 730**

- (Exam Topic 6)

The project manager is dividing the project scope into smaller pieces, and repeating this process until no more subdivisions are required. At this point the project manager is able to estimate costs and activities for each element. What are these elements called?

- A. Project activities
- B. Work packages
- C. Planning packages
- D. Project deliverables

**Answer:** B

#### **NEW QUESTION 735**

- (Exam Topic 6)

Which of the following technology platforms is most effective for sharing information when managing virtual project teams?

- A. Video conferencing
- B. Audio conferencing
- C. Shared portal
- D. Email/chat

**Answer:** D

#### **NEW QUESTION 738**

- (Exam Topic 6)

A project manager is determining the amount of contingency needed for a project. Which analysis is the project manager using?

- A. What-if scenario analysis
- B. Simulation
- C. Alternatives analysis
- D. Reserve analysis

**Answer:** D

#### **NEW QUESTION 740**

- (Exam Topic 6)

In which of the Risk Management processes is the project charter used as an input?

- A. Plan Risk Responses
- B. Implement Risk Responses
- C. Plan Risk Management
- D. Perform Quantitative Risk Responses

**Answer:** C

#### **NEW QUESTION 741**

- (Exam Topic 6)

In which sphere of influence is the project manager demonstrating the value of project management and advancing the efficacy of the project management office (PMO)?

- A. The organization
- B. The project
- C. The industry
- D. The product

**Answer:** B

#### **NEW QUESTION 745**

- (Exam Topic 6)

Analyzing activity sequences, durations, resource requirements, and schedule constraints for project execution and monitoring and controlling relates to which process?

- A. Develop Schedule
- B. Control Schedule
- C. Estimate Activity Durations
- D. Define Activities

**Answer:** A

#### **NEW QUESTION 750**

- (Exam Topic 6)

A project is just beginning, and management creates a long list of potential stakeholders. Which statement about identifying and engaging stakeholders is correct?

- A. The project manager should identify and deal with stakeholders only during the execution phase.
- B. Stakeholder satisfaction should be identified immediately and managed as a project objective.
- C. The project manager should focus on project objectives and deal with stakeholders as a secondary priority.
- D. Stakeholder satisfaction is the most important goal, and project objectives should be considered a secondary priority.

**Answer:** B

**NEW QUESTION 751**

- (Exam Topic 6)

Which statement about identification and engagement of stakeholders during a project is correct?

- A. Project stakeholders should be Identified and engaged in every phase of the project to influence the success of the project directly.
- B. Project stakeholders should be identified and engaged once the prototype is completed to provide their feedback but refrain from making inputs during the project.
- C. Project stakeholders should be identified when the project charter is being completed and engaged during requirements gathering.
- D. Project stakeholders should be identified and engaged during requirements elicitation but not during the Define Scope process.

**Answer:** A

**NEW QUESTION 756**

- (Exam Topic 6)

What does expert judgment provide as an input to the resource management plan?

- A. Geographic distribution of facilities and resources
- B. Physical resource management policies and procedures
- C. Estimated lead times based on lessons learned
- D. Templates for the resource management plan

**Answer:** A

**NEW QUESTION 760**

- (Exam Topic 6)

In an agile and adaptive project, which scope management entity invokes stakeholder engagement?

- A. Collect Requirements
- B. Create work breakdown structure (WBS)
- C. Plan Scope Management
- D. Scope Baseline

**Answer:** A

**NEW QUESTION 762**

- (Exam Topic 6)

A new project manager wishes to recommend creating a project management office to senior management. Which statement would the project manager use to describe the Importance of creating the project management office?

- A. It will give the project manager Independence to make decisions without other departmental input.
- B. It Integrates organizational data and information to ensure that strategic objectives are fulfilled.
- C. The project management office can execute administrative tasks.
- D. The project management office can coordinate projects.

**Answer:** B

**NEW QUESTION 766**

.....

## Thank You for Trying Our Product

### We offer two products:

1st - We have Practice Tests Software with Actual Exam Questions

2nd - Questions and Answers in PDF Format

### CAPM Practice Exam Features:

- \* CAPM Questions and Answers Updated Frequently
- \* CAPM Practice Questions Verified by Expert Senior Certified Staff
- \* CAPM Most Realistic Questions that Guarantee you a Pass on Your First Try
- \* CAPM Practice Test Questions in Multiple Choice Formats and Updates for 1 Year

**100% Actual & Verified — Instant Download, Please Click**  
**[Order The CAPM Practice Test Here](#)**
